ID		Task Name	Duration	Start	Finish	Predecessors	% Complete
1		**Nevada WC System**	**261 days**	**Wed 1/13/16**	**Wed 1/11/17**		**0%**
2		**Identification**	**2 days**	**Wed 1/13/16**	**Thu 1/14/16**		**0%**
13		Pass ID Gate	0 days	Thu 1/14/16	Thu 1/14/16	12	0%
14		**Initiation**	**11 days**	**Fri 1/15/16**	**Fri 1/29/16**		**0%**
28		Pass Initiation Gate	0 days	Fri 1/29/16	Fri 1/29/16	27	0%
29		**Planning**	**27 days**	**Mon 2/1/16**	**Tue 3/8/16**		**0%**
30		**Conduct Client Kickoff Meeting**	**1 day**	**Mon 2/1/16**	**Mon 2/1/16**		**0%**
31		Walk through Kickoff Meeting Slides	1 day	Mon 2/1/16	Mon 2/1/16	28	0%
32		Deliver Welcome Package	1 day	Mon 2/1/16	Mon 2/1/16	28	0%
33		Schedule Working Sessions	1 day	Mon 2/1/16	Mon 2/1/16	28	0%
34		**Define**	**16 days**	**Mon 2/1/16**	**Mon 2/22/16**		**0%**
35		Revise Project Management Plan	1 day	Mon 2/1/16	Mon 2/1/16	28	0%
36		Produce Schedule / Work Breakdown Structure	15 days	Tue 2/2/16	Mon 2/22/16	30,40SS	0%
37		Produce Budget (in Hours in ETC)	15 days	Tue 2/2/16	Mon 2/22/16	30,40SS	0%
38		**Design**	**26 days**	**Tue 2/2/16**	**Tue 3/8/16**		**0%**
51		Pass Preliminary Design Review Gate	0 days	Tue 3/8/16	Tue 3/8/16	50	0%
52		**Execution**	**221 days**	**Wed 3/9/16**	**Wed 1/11/17**		**0%**
53		**Build Activities**	**141 days**	**Wed 3/9/16**	**Wed 9/21/16**		**0%**
54		**Sprint Session1**	**42 days**	**Wed 3/9/16**	**Thu 5/5/16**		**0%**
62		**Sprint Session2**	**42 days**	**Fri 5/6/16**	**Mon 7/4/16**		**0%**
70		**Sprint Session3**	**42 days**	**Tue 7/26/16**	**Wed 9/21/16**		**0%**
78		**Test Activities**	**172 days**	**Wed 3/9/16**	**Thu 11/3/16**		**0%**
79		**Planning**	**10 days**	**Wed 3/9/16**	**Tue 3/22/16**		**0%**
84		**Execution**	**88 days**	**Tue 7/5/16**	**Thu 11/3/16**		**0%**
93		**Deployment Activities**	**49 days**	**Fri 11/4/16**	**Wed 1/11/17**		**0%**
94		**Planning**	**20 days**	**Fri 11/4/16**	**Thu 12/1/16**		**0%**
97		**Execution**	**39 days**	**Fri 11/18/16**	**Wed 1/11/17**		**0%**
103		**Go Live Activities**	**3 days**	**Mon 1/9/17**	**Wed 1/11/17**		**0%**
104		Onboard Users	2 days	Mon 1/9/17	Tue 1/10/17	101	0%
105		Go Live Review	1 day	Wed 1/11/17	Wed 1/11/17	104	0%
106		Pass Go Live Review	1 day	Wed 1/11/17	Wed 1/11/17	104	0%
107		Deploy to PRODUCTION	1 day	Wed 1/11/17	Wed 1/11/17	104	0%
108		**Training**	**17 days**	**Fri 11/4/16**	**Mon 11/28/16**		**0%**
109		**Documentation**	**2 days**	**Fri 11/4/16**	**Mon 11/7/16**		**0%**
110		Finalize User Manual and Administrator Manual	2 days	Fri 11/4/16	Mon 11/7/16	92	0%
111		**Training**	**2 days**	**Fri 11/25/16**	**Mon 11/28/16**		**0%**
112		User Training	1 day	Fri 11/25/16	Fri 11/25/16	99	0%
113		Administrator Training	1 day	Mon 11/28/16	Mon 11/28/16	112	0%
114		**Monitor & Control**	**261 days**	**Wed 1/13/16**	**Wed 1/11/17**		**0%**
169		**Project Required Tasks**	**247 days**	**Mon 2/1/16**	**Wed 1/11/17**		**0%**
170		**5.6 Task 1 - BPR and Detailed Requirements**	**20 days**	**Mon 2/1/16**	**Mon 2/29/16**		**0%**
171		5.6.3.1 - Report of To-Be Business Process	0 days	Mon 2/1/16	Mon 2/1/16	33	0%

ID		Task Name	Duration	Start	Finish	Predecessors	% Complete
172		5.6.3.2 - DIR-WCS detailed system requirements report	0 days	Mon 2/29/16	Mon 2/29/16	45	0%
173		**5.7 Task 2 - System Design/Implementation Configuration**	**0 days**	**Mon 2/29/16**	**Mon 2/29/16**		**0%**
174		5.7.3.1 - System Design Documentation	0 days	Mon 2/29/16	Mon 2/29/16	172	0%
175		5.7.3.2 - Gap/Fit Analysis	0 days	Mon 2/29/16	Mon 2/29/16	174	0%
176		**5.8 Task 3 - Build and Implement System**	**0 days**	**Thu 10/6/16**	**Thu 10/6/16**		**0%**
177		5.8.3.1 - Demo of System Components	0 days	Thu 10/6/16	Thu 10/6/16	91	0%
178		5.8.3.2 - Deliver Fully Functional System	0 days	Thu 10/6/16	Thu 10/6/16	177	0%
179		5.8.3.3 - Walk through of entire system prior to UAT	0 days	Thu 10/6/16	Thu 10/6/16	91	0%
180		**5.9 Task 4 - Data Migration**	**0 days**	**Thu 12/1/16**	**Thu 12/1/16**		**0%**
181		5.9.3.1 - Detailed data migration plan	0 days	Thu 12/1/16	Thu 12/1/16	96	0%
182		5.9.3.2 - Test cases for validating converted data	0 days	Thu 12/1/16	Thu 12/1/16	96	0%
183		5.9.3.3. - Migrate data to test and production	0 days	Thu 12/1/16	Thu 12/1/16	96	0%
184		**5.10 Task 5 - User Acceptance Testing**	**0 days**	**Thu 10/6/16**	**Thu 10/6/16**		**0%**
185		5.10.3.1 - Test Environment (Vendor to perform Testing)	0 days	Thu 10/6/16	Thu 10/6/16	91	0%
186		5.10.3.2 - Vendor training of UAT team	0 days	Thu 10/6/16	Thu 10/6/16	91	0%
187		5.10.3.3. - Review of DIR-WCS's UAT plan	0 days	Thu 10/6/16	Thu 10/6/16	91	0%
188		5.10.3.4 - Technical support and timely remediation	0 days	Thu 10/6/16	Thu 10/6/16	91	0%
189		**5.11 Task 6 - Documentation**	**0 days**	**Mon 11/7/16**	**Mon 11/7/16**		**0%**
190		5.11.3.1 - User Manual	0 days	Mon 11/7/16	Mon 11/7/16	110	0%
191		5.11.3.2 - Online help functionality and content	0 days	Mon 11/7/16	Mon 11/7/16	110	0%
192		5.11.3.3 - System administration/operations guide	0 days	Mon 11/7/16	Mon 11/7/16	110	0%
193		5.11.3.4 - Technical System Design Report	0 days	Mon 11/7/16	Mon 11/7/16	110	0%
194		**5.12 Task 7 - Training**	**13 days**	**Mon 11/7/16**	**Thu 11/24/16**		**0%**
195		5.12.3.1 - Training Plan	0 days	Mon 11/7/16	Mon 11/7/16	192	0%
196		5.12.3.2 - Training materials and scenarios	0 days	Thu 11/24/16	Thu 11/24/16	99	0%
197		5.12.3.3 - Fully functional training environment with data	0 days	Thu 11/24/16	Thu 11/24/16	99	0%
198		5.12.3.4 - Training	0 days	Thu 11/24/16	Thu 11/24/16	99	0%
199		**5.13 Task 8 - Transition to Production**	**0 days**	**Thu 11/24/16**	**Thu 11/24/16**		**0%**
200		5.13.3.1 - Production transition plan	0 days	Thu 11/24/16	Thu 11/24/16	198	0%
201		5.13.3.2 - Final conversion of legacy data to new system	0 days	Thu 11/24/16	Thu 11/24/16	200	0%
202		5.13.3.3 - Technical support after go-live for at least two weeks	0 days	Thu 11/24/16	Thu 11/24/16	201	0%
203		**5.14 Task 9 - Post Implementation Review**	**0 days**	**Wed 1/11/17**	**Wed 1/11/17**		**0%**
204		5.14.3.1 Post Implementation Review Plan	0 days	Wed 1/11/17	Wed 1/11/17	107	0%
205		5.14.3.2 Execute Plan	0 days	Wed 1/11/17	Wed 1/11/17	204	0%
206		5.14.3.3 Resolution of Vendor and System Operational Issues	0 days	Wed 1/11/17	Wed 1/11/17	205	0%
207		**5.15 Task 10 - Warranty and Corrective Maintenance**	**0 days**	**Wed 1/11/17**	**Wed 1/11/17**		**0%**
208		5.15.3.1 Timely corrective action on all system defects	0 days	Wed 1/11/17	Wed 1/11/17	206	0%
209		5.15.3.2 User Support	0 days	Wed 1/11/17	Wed 1/11/17	208	0%
210		5.15.3.3. Release Notes	0 days	Wed 1/11/17	Wed 1/11/17	209	0%

Deliverable Number	Task Number
5.6	**1**
5.6.3.1	1

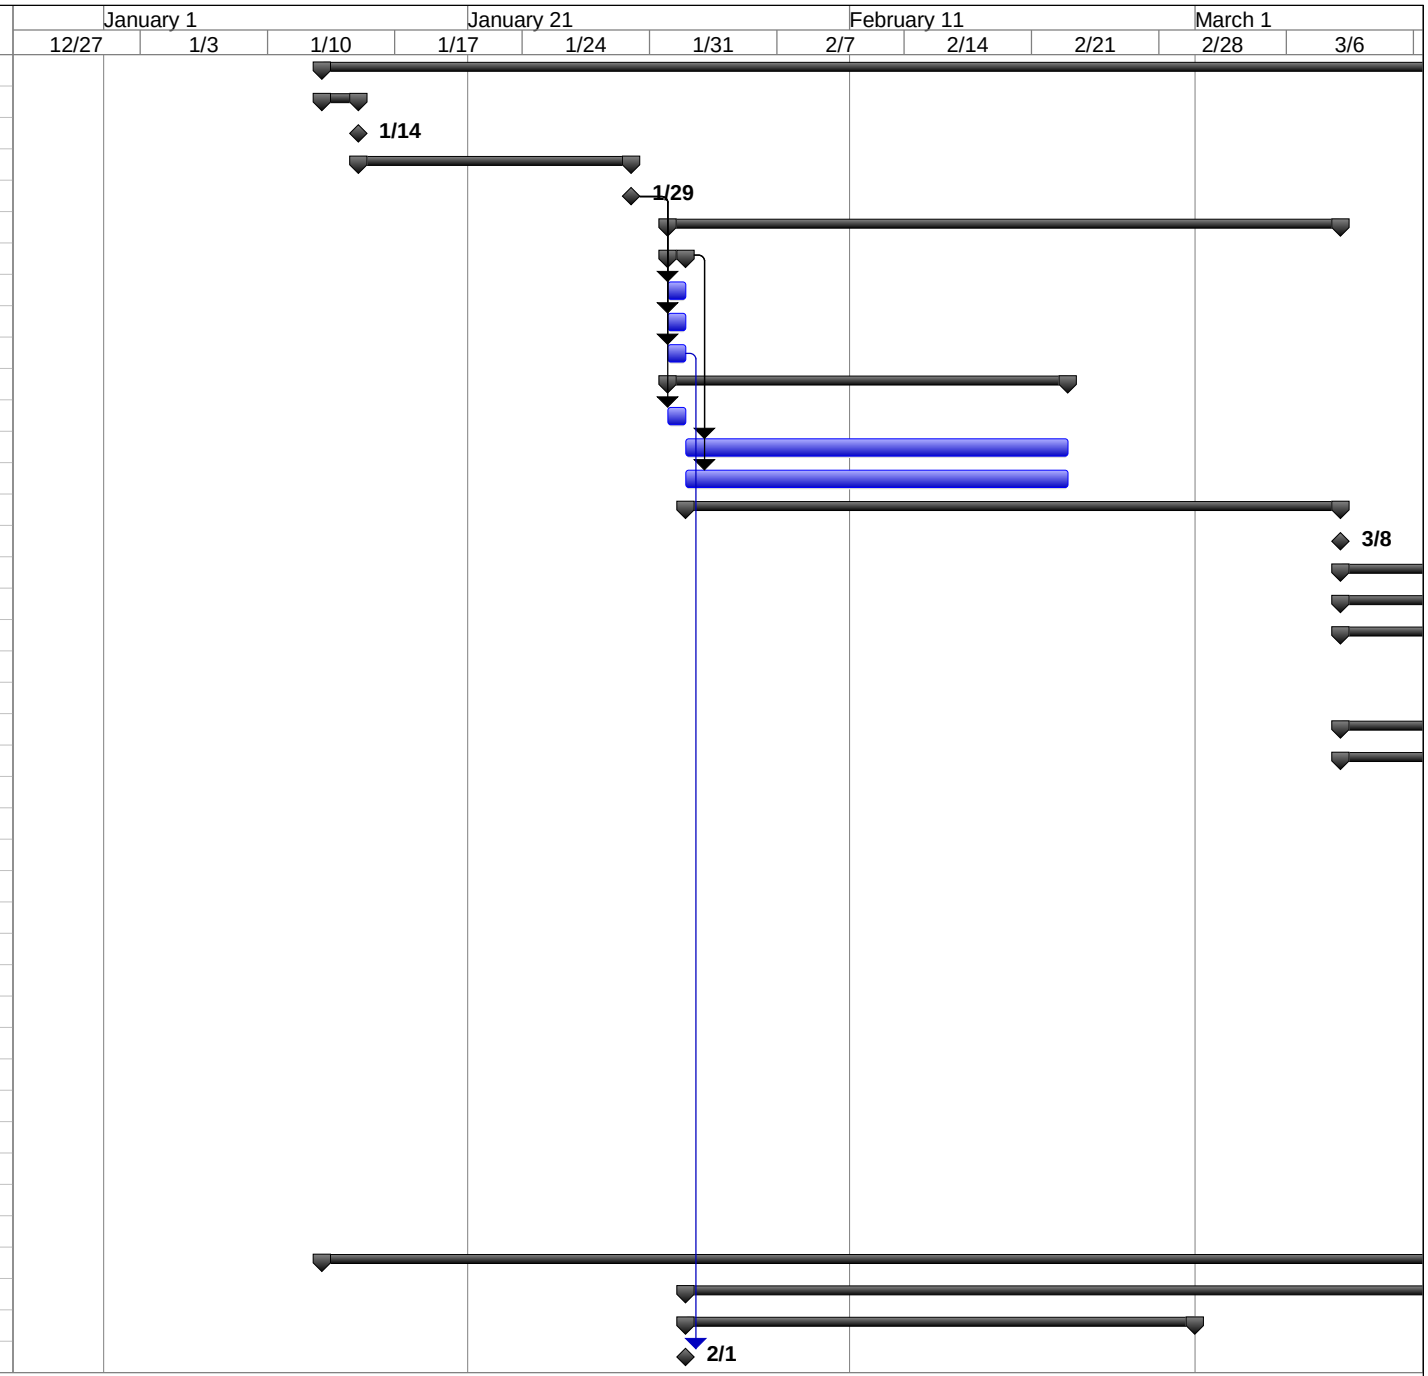

Deliverable Number	Task Number	January 1				January 21			February 11		March 1	
		12/27	1/3	1/10	1/17	1/24	1/31	2/7	2/14	2/21	2/28	3/6
5.6.3.2	1										**2/29**	
5.7	**2**										**2/29**	
5.7.3.1	2										**2/29**	
5.7.3.2	2										**2/29**	
5.8	**3**											
5.8.3.1	3											
5.8.3.2	3											
5.8.3.3	3											
5.9	**4**											
5.9.3.1	4											
5.9.3.2	4											
5.9.3.3	4											
5.10	**5**											
5.10.3.1	5											
5.10.3.2	5											
5.10.3.3	5											
5.10.3.4	5											
5.11	**6**											
5.11.3.1	6											
5.11.3.2	6											
5.11.3.3	6											
5.11.3.4	6											
5.12	**7**											
5.12.3.1	7											
5.12.3.2	7											
5.12.3.3	7											
5.12.3.4	7											
5.13	**8**											
5.13.3.1	8											
5.13.3.2	8											
5.13.3.3	8											
5.14	**9**											
5.14.3.1	9											
5.14.3.2	9											
5.14.3.3	9											
5.15	**10**											
5.15.3.1	10											
5.15.3.2	10											
5.15.3.3	10											

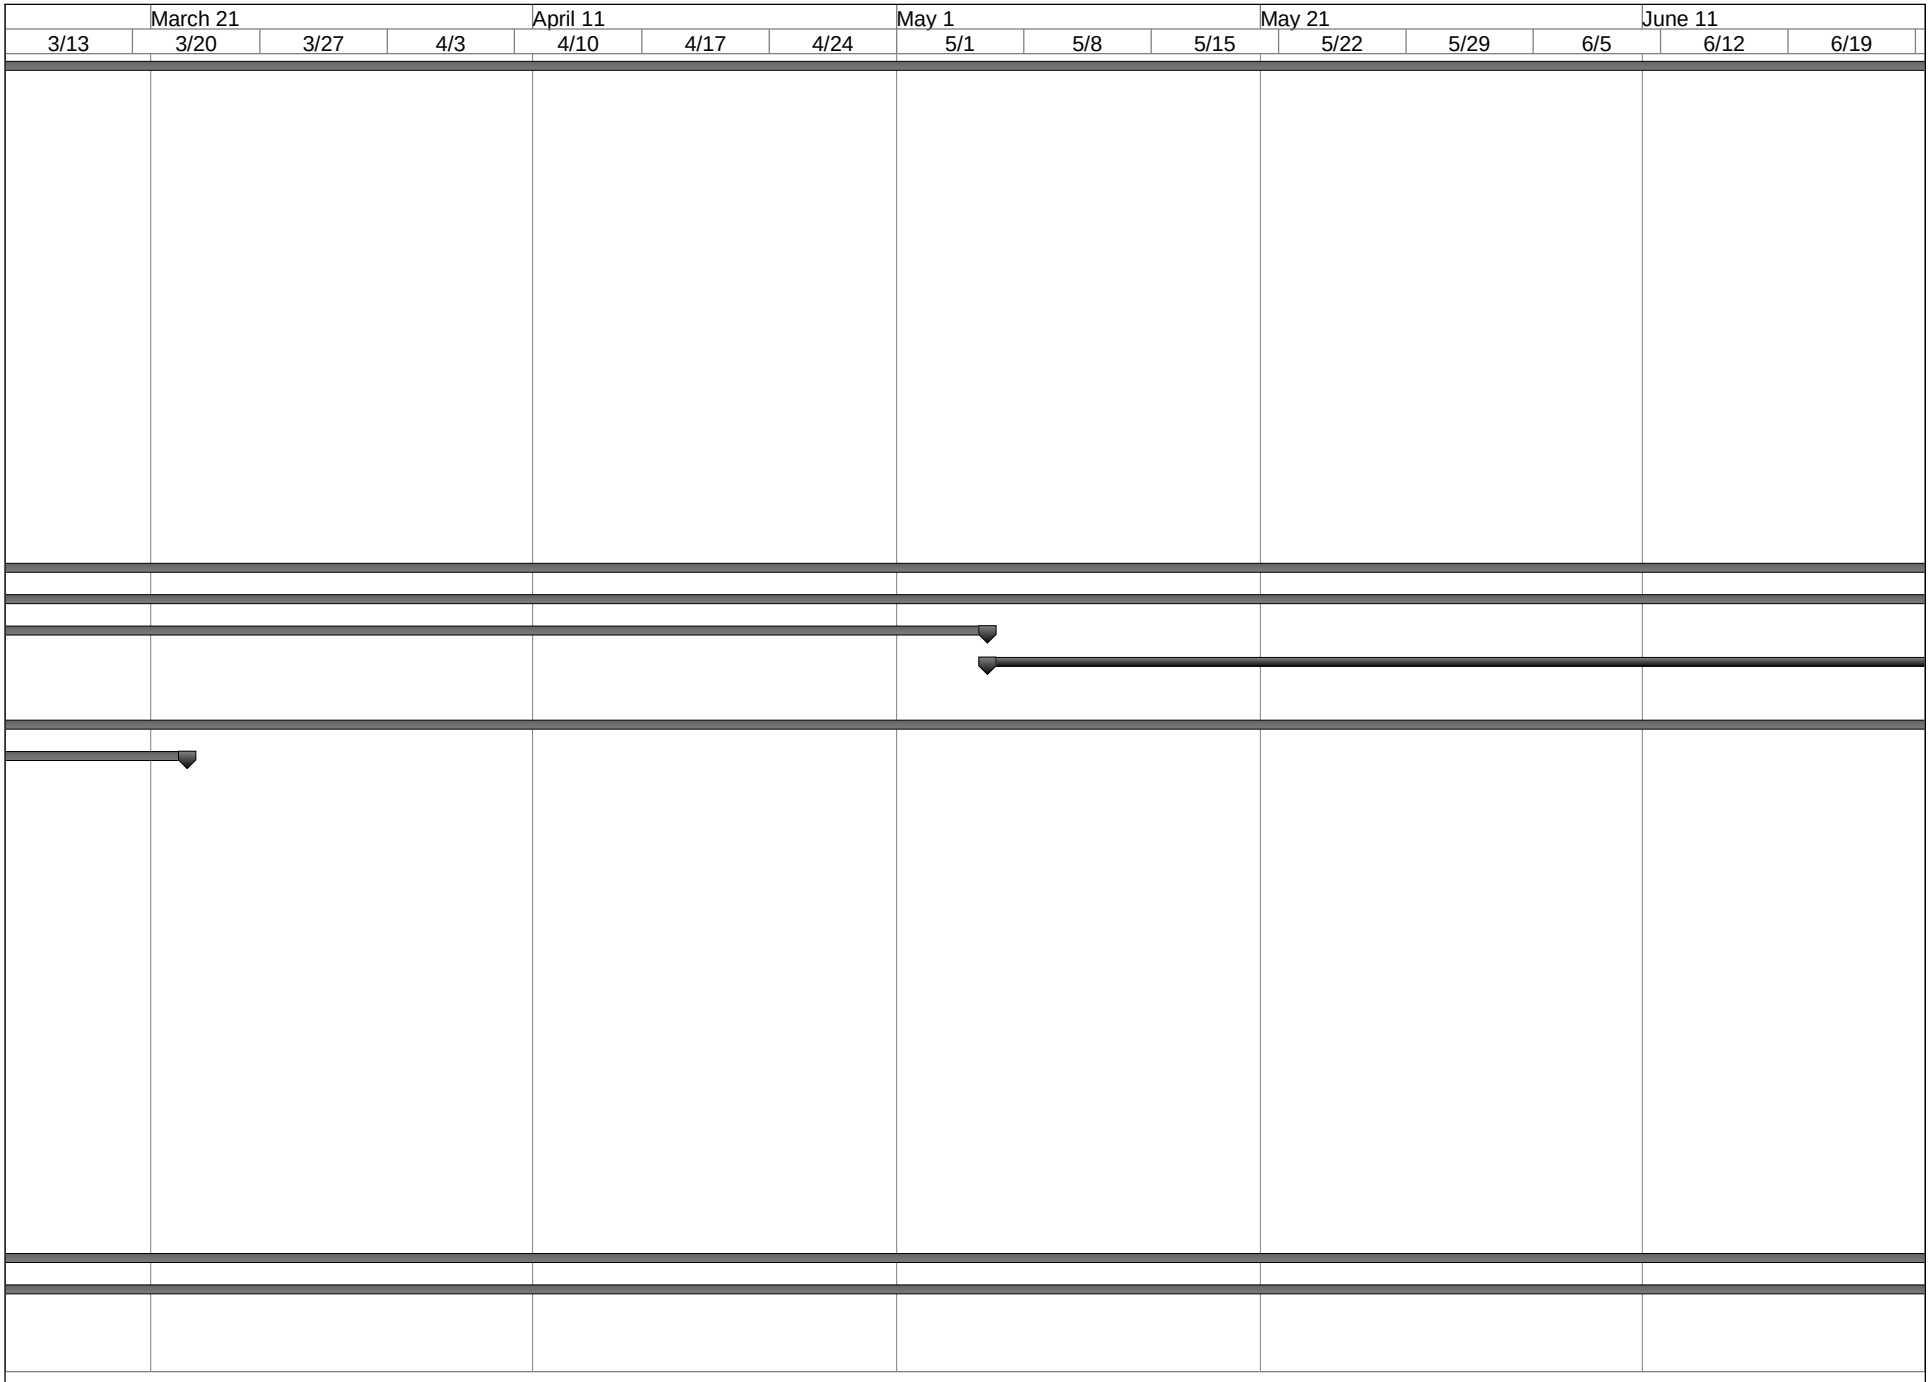
March 21
April 11
May 1
May 21
June 11
3/13
3/20
3/27
4/3
4/10
4/17
4/24
5/1
5/8
5/15
5/22
5/29
6/5
6/12
6/19

	March 21			April 11			May 1			May 21			June 11	
3/13	3/20	3/27	4/3	4/10	4/17	4/24	5/1	5/8	5/15	5/22	5/29	6/5	6/12	6/19

July 1
July 21
August 11
September 1
September 21
6/26
7/3
7/10
7/17
7/24
7/31
8/7
8/14
8/21
8/28
9/4
9/11
9/18
9/25
10/2

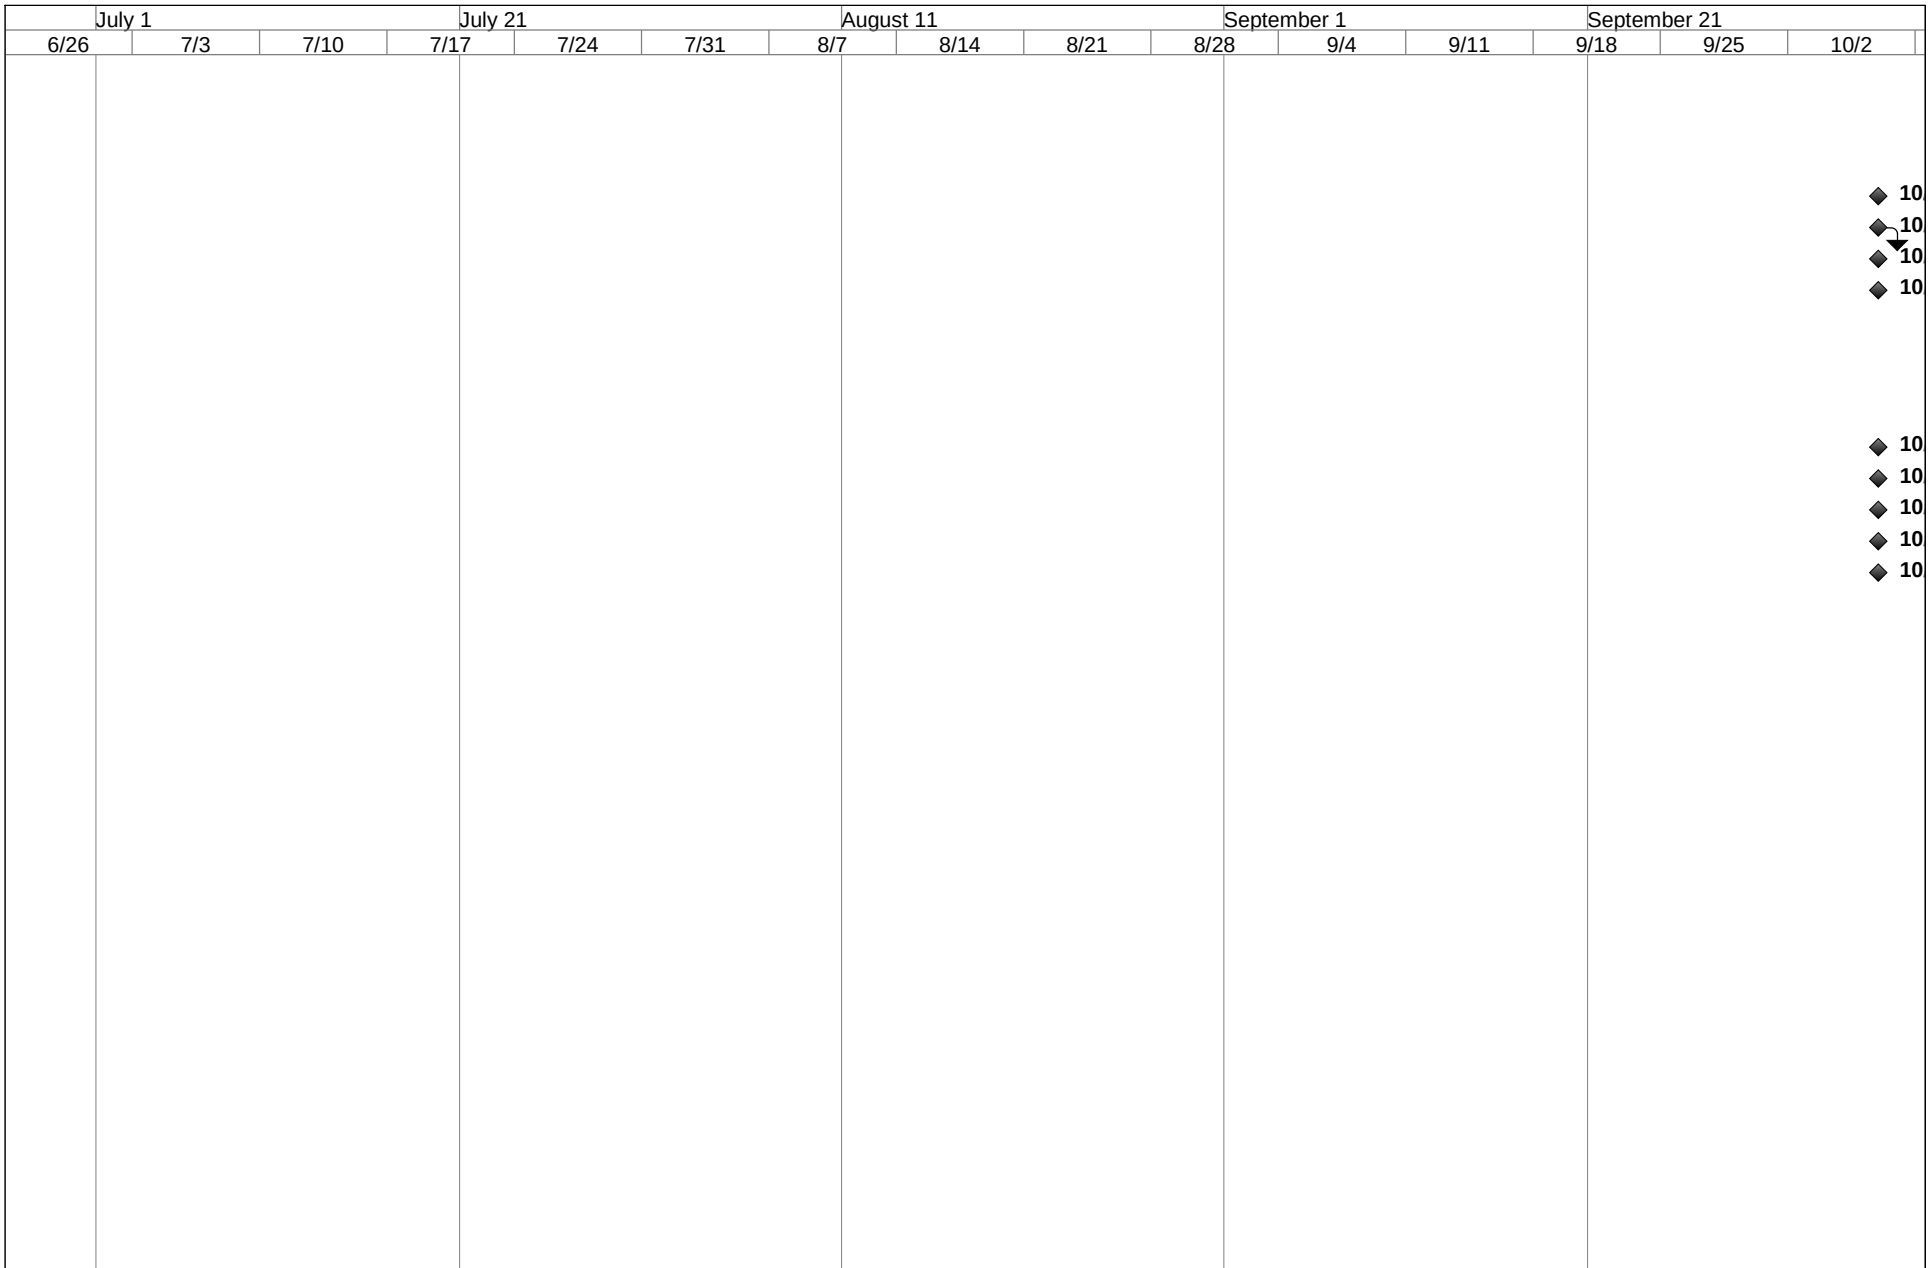
July 1
July 21
August 11
September 1
September 21
6/26
7/3
7/10
7/17
7/24
7/31
8/7
8/14
8/21
8/28
9/4
9/11
9/18
9/25
10/2
10
10
10
10
10
10
10
10
10

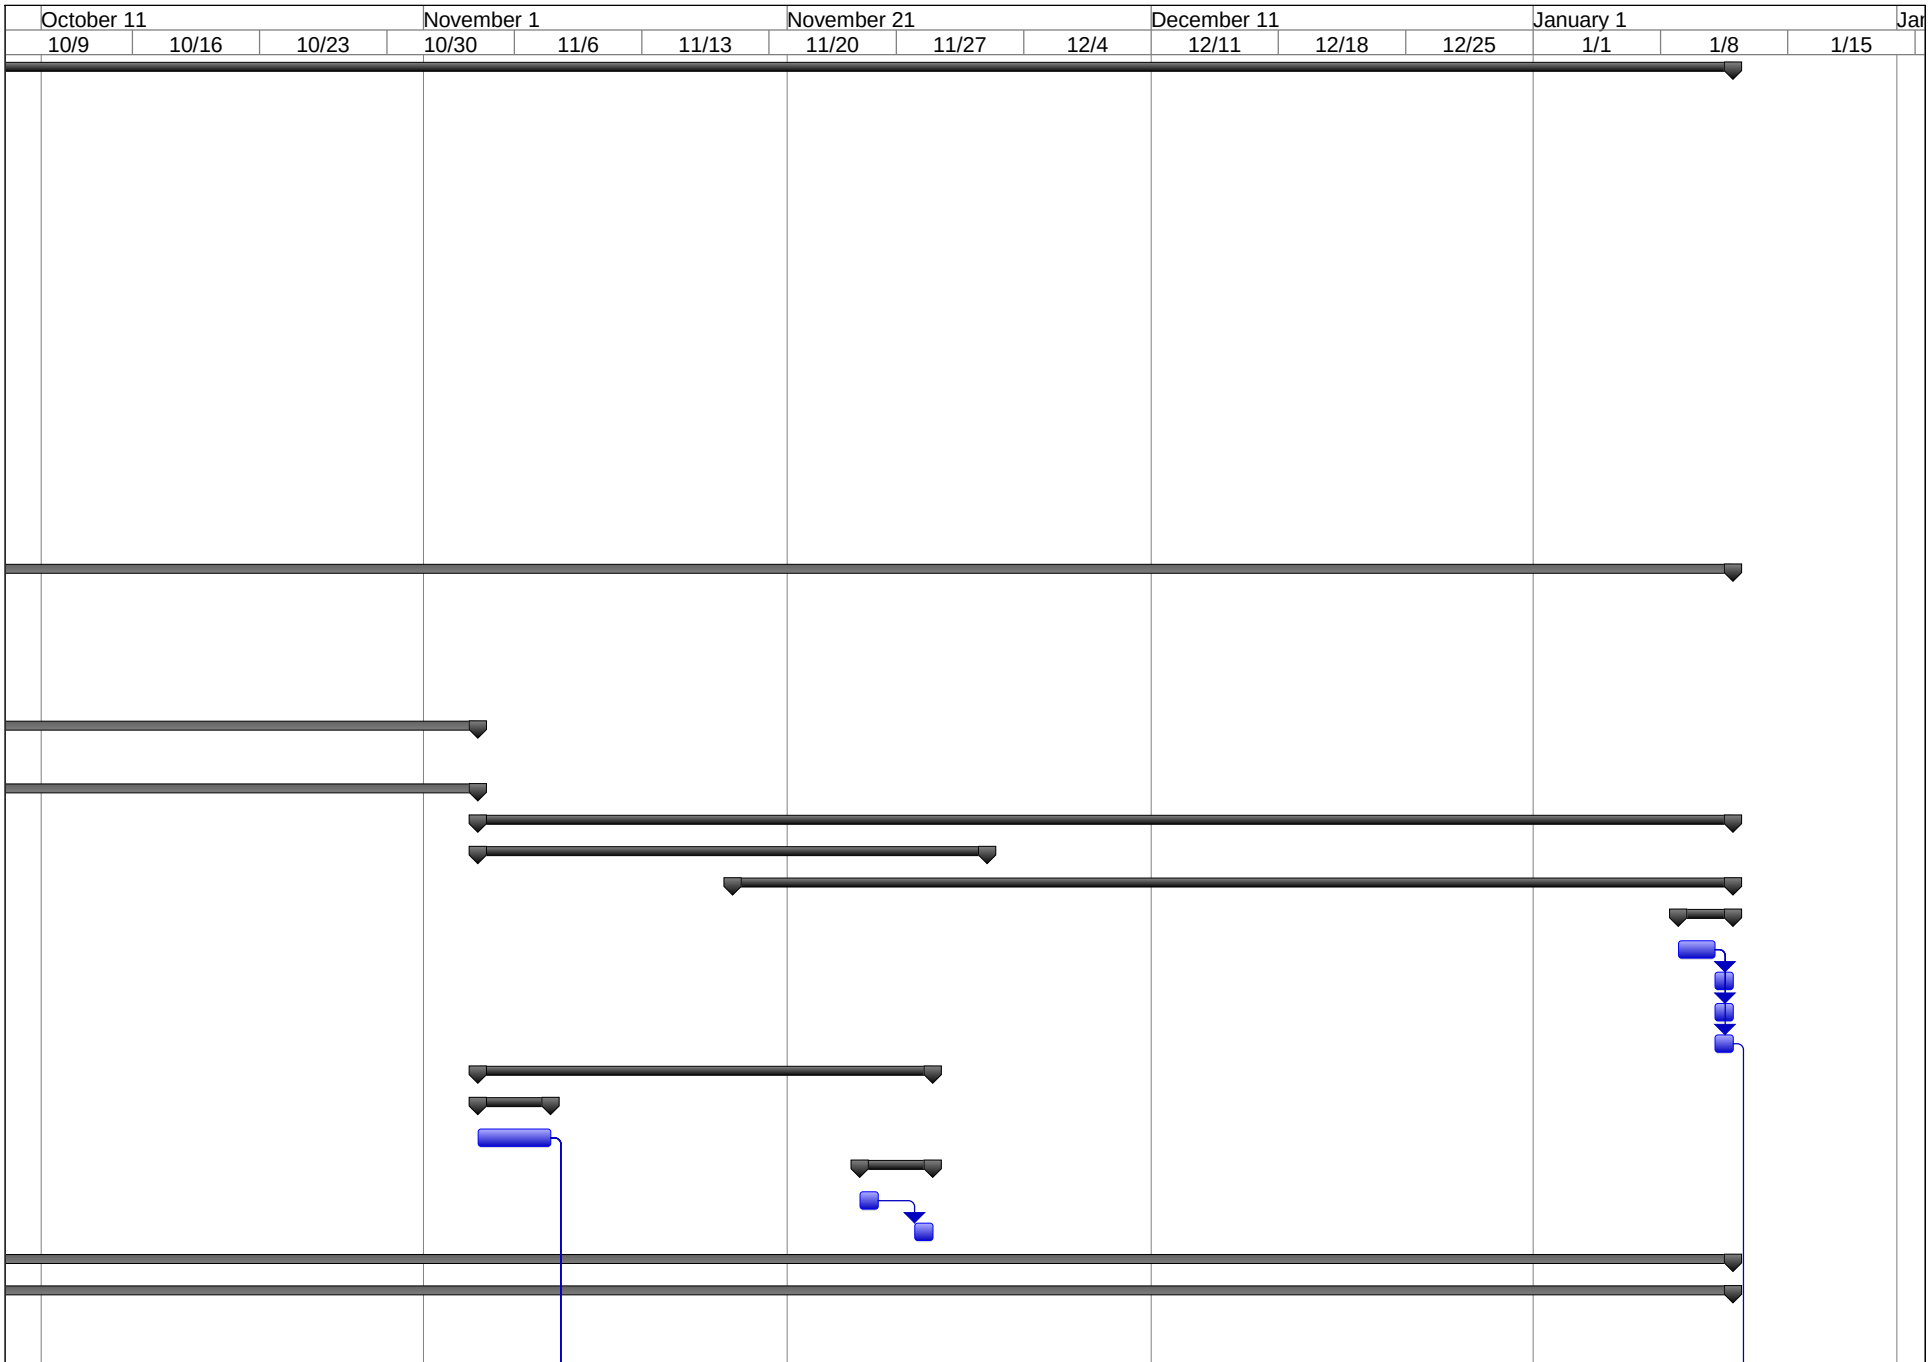
October 11
November 1
November 21
December 11
January 1
Jan
10/9
10/16
10/23
10/30
11/6
11/13
11/20
11/27
12/4
12/11
12/18
12/25
1/1
1/8
1/15

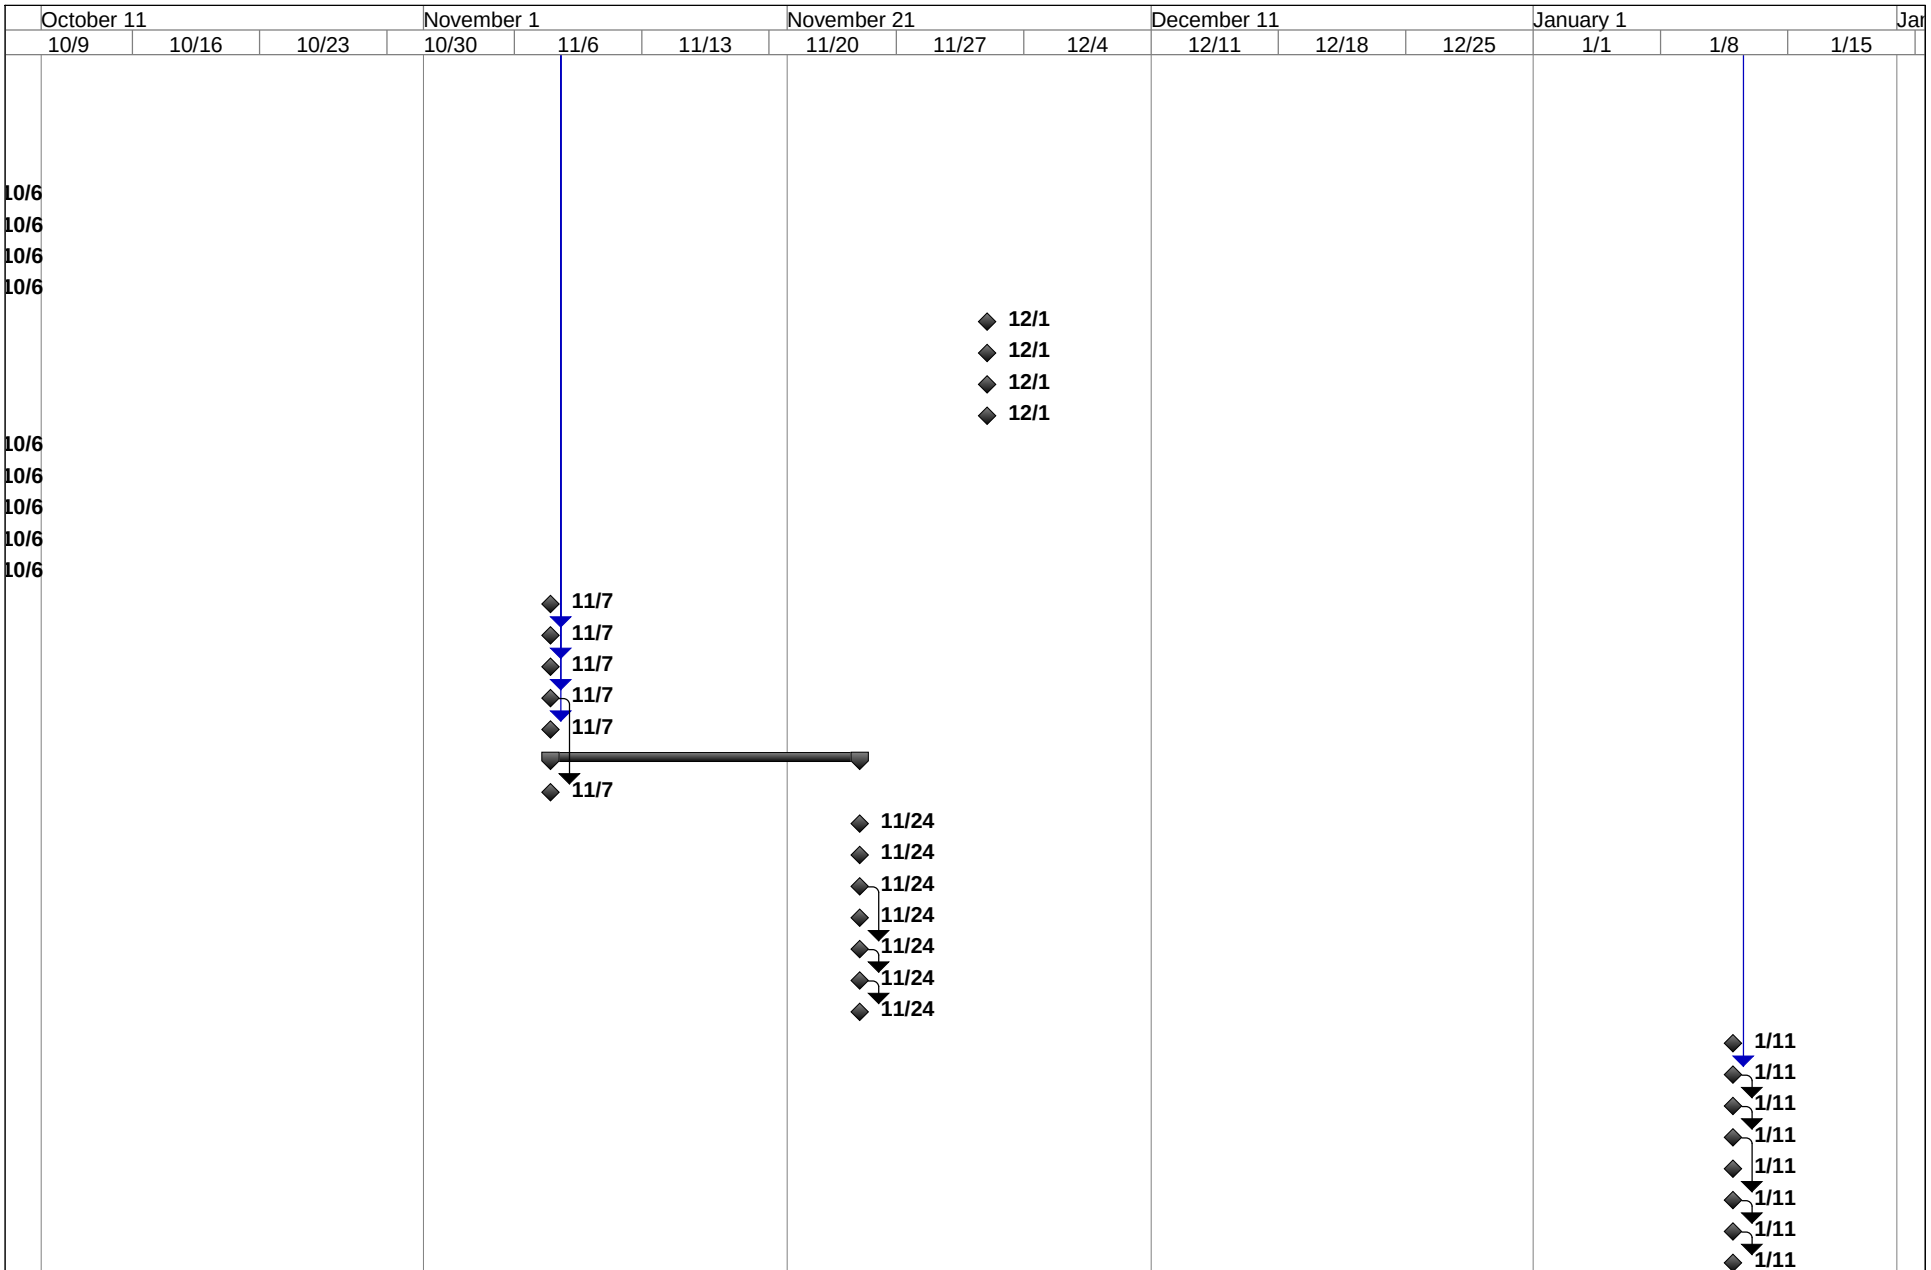
October 11
November 1
November 21
December 11
January 1
Jan
10/9
10/16
10/23
10/30
11/6
11/13
11/20
11/27
12/4
12/11
12/18
12/25
1/1
1/8
1/15
10/6
10/6
10/6
10/6
12/1
12/1
12/1
12/1
10/6
10/6
10/6
10/6
10/6
11/7
11/7
11/7
11/7
11/7
11/7
11/24
11/24
11/24
11/24
11/24
11/24
11/24
1/11
1/11
1/11
1/11
1/11
1/11
1/11
1/11
